| Activity ID | Activity Description | OD | RD | % | ES | EF | TF |
|---|---|---|---|---|---|---|---|
| 1 | NTP | 0 | 0 | 0 | 29MAY07* | | 0 |
| 1900 | SFA - EROSION CONTROL | 5 | 5 | 0 | 29MAY07 | 04JUN07 | 0 |
| 2900 | R/A - EROSION CONTROL | 30 | 30 | 0 | 05JUN07 | 04JUL07 | 0 |
| 3900 | F&D - EROSION CONTROL | 1 | 1 | 0 | 05JUL07 | 05JUL07 | 0 |
| 5010 | INSTALL SEDIMENT EROSION CONTOL | 4 | 4 | 0 | 06JUL07 | 11JUL07 | 0 |
| 5020 | INSPECT SEDIMENT EROSION CONTOL | 1 | 1 | 0 | 12JUL07 | 12JUL07 | 0 |
| 5030 | DEMOLITION | 5 | 5 | 0 | 13JUL07 | 20JUL07 | 0 |
| 5040 | INSTALL SHORING | 10 | 10 | 0 | 23JUL07 | 06AUG07 | 0 |
| 5050 | MASS EXCAVATION | 5 | 5 | 0 | 01AUG07 | 07AUG07 | 0 |
| 6000 | F/R/P PERIMETER FOOTINGS (NORTH) | 5 | 5 | 0 | 09AUG07 | 15AUG07 | 0 |
| 6010 | F/R/P PERIMETER FOOTING (EAST) | 8 | 8 | 0 | 16AUG07 | 28AUG07 | 0 |
| 6020 | F/R/P PERIMETER FOOTING (SOUTH) | 5 | 5 | 0 | 29AUG07 | 05SEP07 | 0 |
| 6030 | F/R/P PERIMETER FOOTINGS (WEST) | 6 | 6 | 0 | 06SEP07 | 14SEP07 | 0 |
| 6040 | F/R/P INTERIOR FOOTINGS & GRADE BEAMS | 5 | 5 | 0 | 17SEP07 | 21SEP07 | 0 |
| 6050 | U.G. ELECTRICAL | 2 | 2 | 0 | 24SEP07 | 25SEP07 | 0 |
| 6060 | U.G. PLUMBING | 3 | 3 | 0 | 24SEP07 | 27SEP07 | 0 |
| 6070 | F/R/P CONC WALLS (NORTH) | 5 | 5 | 0 | 28SEP07 | 04OCT07 | 0 |
| 6080 | F/R/P CONC WALLS (EAST) | 8 | 8 | 0 | 05OCT07 | 17OCT07 | 0 |
| 6090 | F/R/P CONC WALLS (SOUTH) | 5 | 5 | 0 | 18OCT07 | 25OCT07 | 0 |
| 6100 | F/R/P CONC WALLS (WEST) | 7 | 7 | 0 | 26OCT07 | 05NOV07 | 0 |
| 8460 | WATERPROOF PERIMETER WALLS | 5 | 5 | 0 | 06NOV07 | 13NOV07 | 0 |
| 6110 | SOG PREP. (STONE, MESH & VAPOR BARRIER) | 2 | 2 | 0 | 15NOV07 | 16NOV07 | 0 |
| 6120 | F/R/P SOG | 5 | 5 | 0 | 19NOV07 | 27NOV07 | 0 |
| 6130 | CMU BLOCK @ ELEVATOR SHAFT | 10 | 10 | 0 | 29NOV07 | 13DEC07 | 0 |
| 6180 | 1ST FLOOR F/R/P SOD | 4 | 4 | 0 | 14DEC07 | 20DEC07 | 0 |
| 6190 | 1ST FLOOR STEEL COLUMNS | 3 | 3 | 0 | 21DEC07 | 27DEC07 | 0 |
| 6200 | 1ST FLOOR STEEL BEAMS | 3 | 3 | 0 | 03JAN08 | 07JAN08 | 0 |
| 6210 | 1ST FLOOR STEEL JOISTS | 3 | 3 | 0 | 08JAN08 | 11JAN08 | 0 |
| 6220 | 1ST FLOOR STEEL DECKING | 3 | 3 | 0 | 14JAN08 | 17JAN08 | 0 |
| 6230 | 2ND FLOOR F/R/P SOD | 4 | 4 | 0 | 18JAN08 | 24JAN08 | 0 |
| 6240 | 2ND FLOOR STEEL COLUMNS | 3 | 3 | 0 | 25JAN08 | 29JAN08 | 0 |
| 6250 | 2ND FLOOR STEEL BEAMS | 3 | 3 | 0 | 31JAN08 | 04FEB08 | 0 |
| 6260 | 2ND FLOOR STEEL JOISTS | 3 | 3 | 0 | 05FEB08 | 08FEB08 | 0 |
| 6270 | 2ND FLOOR STEEL DECKING | 3 | 3 | 0 | 11FEB08 | 15FEB08 | 0 |
| 6280 | 3RD FLOOR F/R/P SOD | 5 | 5 | 0 | 18FEB08 | 25FEB08 | 0 |
| 6290 | 3RD FLOOR STEEL COLUMNS | 3 | 3 | 0 | 26FEB08 | 29FEB08 | 0 |
| 6300 | 3RD FLOOR STEEL BEAMS | 3 | 3 | 0 | 03MAR08 | 06MAR08 | 0 |

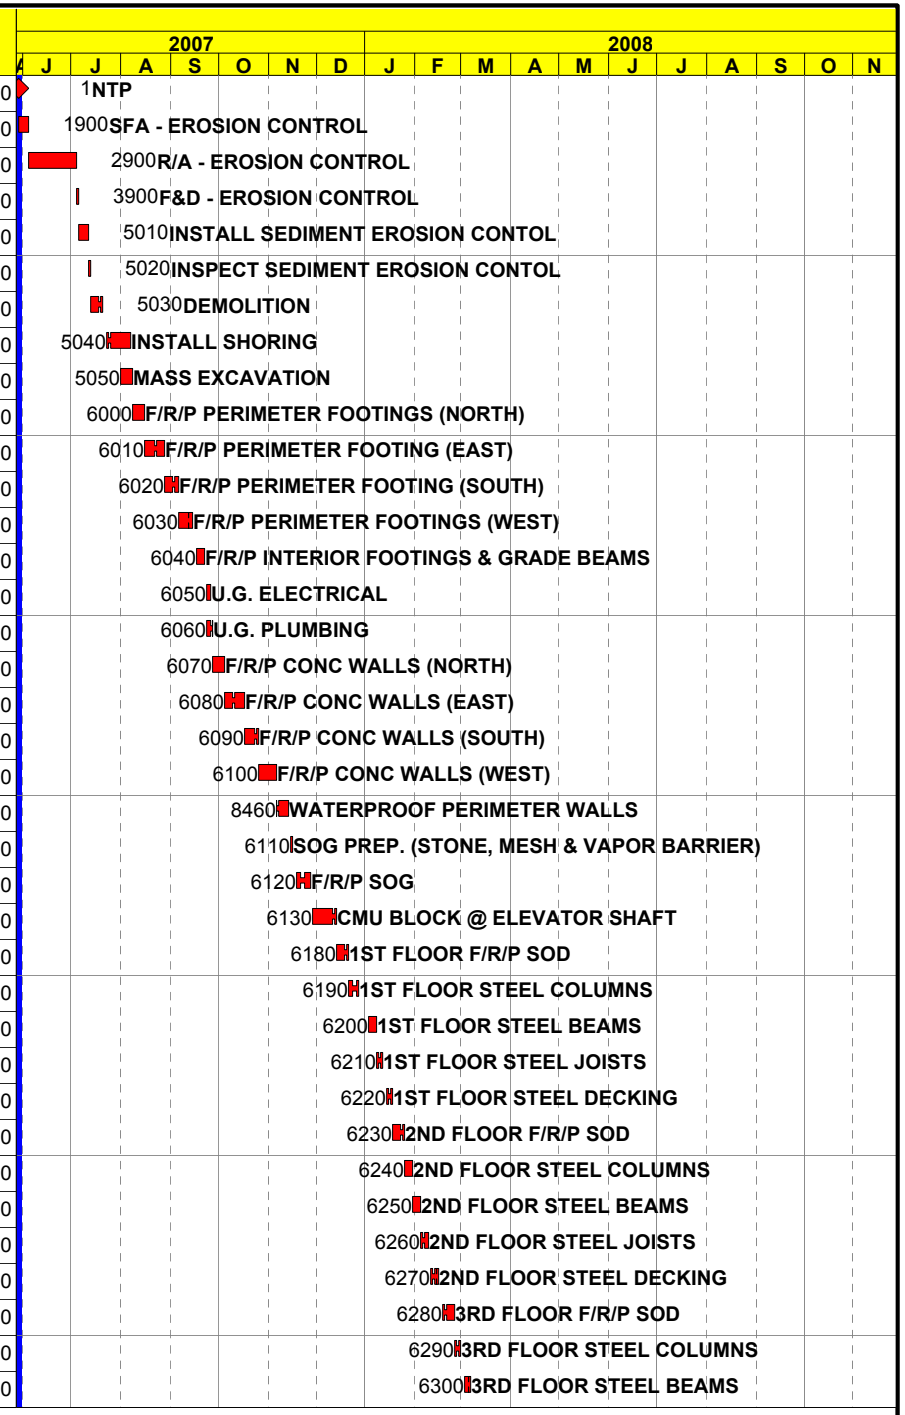


| | |
|---|---|
| Start Date | 01MAY07 |
| Finish Date | 07NOV08 |
| Data Date | 29MAY07 |
| Run Date | 21MAR08 13:19 |

Early Bar
Progress Bar
Critical Activity

WC00

Sheet 1 of 3

**SIMSONA CORP.**

**SENIOR WELLNESS CENTER - WARD 1**
**BASELINE**
**LONGEST PATH**

| Date | Revision | Checked | Approved |
|---|---|---|---|
| | | | |

© Primavera Systems, Inc.

| Activity ID | Activity Description | OD | RD | % | ES | EF | TF |
|---|---|---|---|---|---|---|---|
| 6310 | 3RD FLOOR STEEL JOISTS | 3 | 3 | 0 | 07MAR08 | 12MAR08 | 0 |
| 6320 | 3RD FLOOR STEEL DECKING | 3 | 3 | 0 | 14MAR08 | 18MAR08 | 0 |
| 6990 | BASEMENT R/I OH HVAC DUCTS | 5 | 5 | 0 | 19MAR08 | 25MAR08 | 0 |
| 7000 | BASEMENT R/I OH MECHANICAL PIPING | 5 | 5 | 0 | 26MAR08 | 01APR08 | 0 |
| 7260 | 1ST FLOOR R/I OH HVAC DUCTS | 5 | 5 | 0 | 26MAR08 | 01APR08 | 0 |
| 7010 | BASEMENT R/I OH PLUMBING PIPING | 5 | 5 | 0 | 02APR08 | 08APR08 | 0 |
| 7270 | 1ST FLOOR R/I OH MECHANICAL PIPING | 5 | 5 | 0 | 02APR08 | 08APR08 | 0 |
| 7610 | 2ND FLOOR R/I OH HVAC DUCTS | 5 | 5 | 0 | 02APR08 | 08APR08 | 0 |
| 7020 | BASEMENT R/I OH ELECTRIC | 5 | 5 | 0 | 09APR08 | 15APR08 | 0 |
| 7280 | 1ST FLOOR R/I OH PLUMBING | 5 | 5 | 0 | 09APR08 | 15APR08 | 0 |
| 7620 | 2ND FLOOR R/I OH MECHANICAL PIPING | 5 | 5 | 0 | 09APR08 | 15APR08 | 0 |
| 7030 | BASEMENT R/I OH SPRINKLER | 5 | 5 | 0 | 16APR08 | 22APR08 | 0 |
| 7290 | 1ST FLOOR R/I OH ELECTRIC | 5 | 5 | 0 | 16APR08 | 22APR08 | 0 |
| 7630 | 2ND FLOOR R/I OH PLUMBING | 5 | 5 | 0 | 16APR08 | 22APR08 | 0 |
| 7040 | BASEMENT SET DOOR FRAMES | 3 | 3 | 0 | 23APR08 | 25APR08 | 0 |
| 7300 | 1ST FLOOR R/I OH SPRINKLER | 5 | 5 | 0 | 23APR08 | 29APR08 | 0 |
| 7640 | 2ND FLOOR R/I OH ELECTRIC | 5 | 5 | 0 | 23APR08 | 29APR08 | 0 |
| 7050 | BASEMENT FRAME WALLS AND BLOCKING | 5 | 5 | 0 | 28APR08 | 02MAY08 | 0 |
| 7310 | 1ST FLOOR SET DOOR FRAMES | 3 | 3 | 0 | 30APR08 | 02MAY08 | 0 |
| 7650 | 2ND FLOOR R/I OH SPRINKLER | 5 | 5 | 0 | 30APR08 | 06MAY08 | 0 |
| 7320 | 1ST FLOOR FRAME WALLS AND BLOCKING | 5 | 5 | 0 | 05MAY08 | 09MAY08 | 0 |
| 7660 | 2ND FLOOR SET DOOR FRAMES | 3 | 3 | 0 | 07MAY08 | 09MAY08 | 0 |
| 7670 | 2ND FLOOR FRAME WALLS AND BLOCKING | 5 | 5 | 0 | 12MAY08 | 16MAY08 | 0 |
| 7680 | 2ND FLOOR OPERABLE WALL PARTITION RAILS | 2 | 2 | 0 | 19MAY08 | 20MAY08 | 0 |
| 7690 | 2ND FLOOR DRYWALL 1ST SIDE | 5 | 5 | 0 | 21MAY08 | 28MAY08 | 0 |
| 7700 | 2ND FLOOR R/I WALL PLUMBING | 5 | 5 | 0 | 29MAY08 | 04JUN08 | 0 |
| 7710 | 2ND FLOOR R/I WALL ELECTRIC | 5 | 5 | 0 | 05JUN08 | 11JUN08 | 0 |
| 8060 | 3RD FLOOR R/I WALL PLUMBING | 5 | 5 | 0 | 05JUN08 | 11JUN08 | 0 |
| 7720 | 2ND FLOOR CLOSE IN INSPECTIONS | 4 | 4 | 0 | 12JUN08 | 17JUN08 | 0 |
| 8070 | 3RD FLOOR R/I WALL ELECTRIC | 5 | 5 | 0 | 12JUN08 | 18JUN08 | 0 |
| 7730 | 2ND FLOOR INSULATION | 5 | 5 | 0 | 18JUN08 | 24JUN08 | 0 |
| 8080 | 3RD FLOOR CLOSE IN INSPECTIONS | 4 | 4 | 0 | 19JUN08 | 24JUN08 | 0 |
| 7740 | 2ND FLOOR DRYWALL 2ND SIDE | 5 | 5 | 0 | 25JUN08 | 01JUL08 | 0 |
| 8090 | 3RD FLOOR INSULATION | 5 | 5 | 0 | 25JUN08 | 01JUL08 | 0 |
| 7750 | 2ND FLOOR DRYWALL CEILING | 5 | 5 | 0 | 02JUL08 | 09JUL08 | 0 |
| 8100 | 3RD FLOOR DRYWALL 2ND SIDE | 5 | 5 | 0 | 02JUL08 | 09JUL08 | 0 |
| 7760 | 2ND FLOOR TAPE AND FINISH DRYWALL | 5 | 5 | 0 | 10JUL08 | 16JUL08 | 0 |

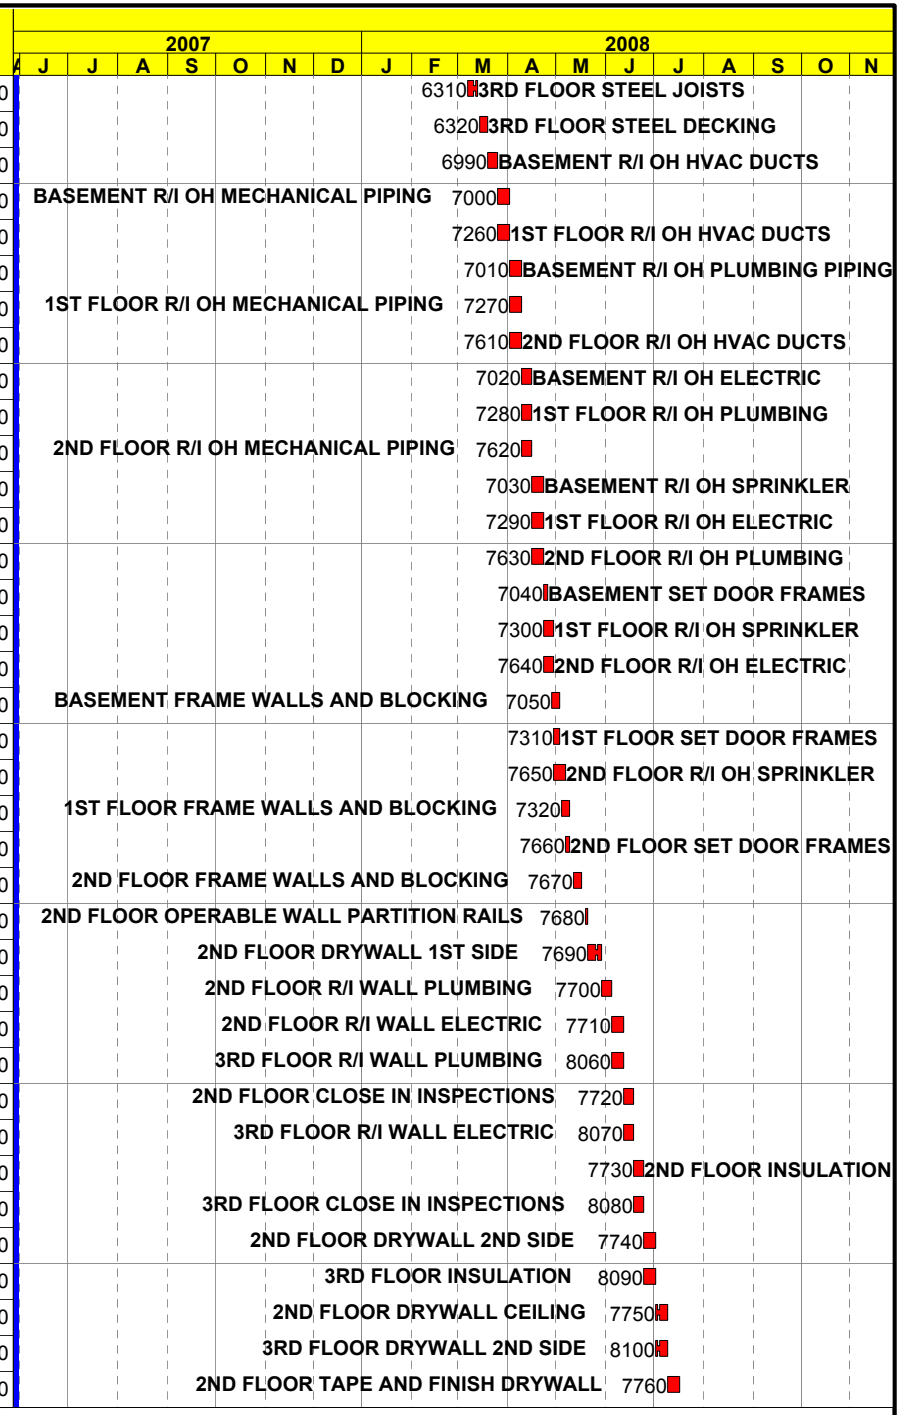


| | |
|---|---|
| Start Date | 01MAY07 |
| Finish Date | 07NOV08 |
| Data Date | 29MAY07 |
| Run Date | 21MAR08 13:19 |

Early Bar
Progress Bar
Critical Activity

WC00

Sheet 2 of 3

**SIMSONA CORP.**

**SENIOR WELLNESS CENTER - WARD 1**
**BASELINE**
**LONGEST PATH**

| Date | Revision | Checked | Approved |
|---|---|---|---|

© Primavera Systems, Inc.

| Activity ID | Activity Description | OD | RD | % | ES | EF | TF |
|---|---|---|---|---|---|---|---|
| 8110 | 3RD FLOOR DRYWALL CEILING | 5 | 5 | 0 | 10JUL08 | 16JUL08 | 0 |
| 7770 | 2ND FLOOR BATHROOM TILE FLOOR | 4 | 4 | 0 | 17JUL08 | 22JUL08 | 0 |
| 8120 | 3RD FLOOR TAPE AND FINISH DRYWALL | 5 | 5 | 0 | 17JUL08 | 23JUL08 | 0 |
| 7780 | 2ND FLOOR BATHROOM TILE WALLS | 5 | 5 | 0 | 23JUL08 | 29JUL08 | 0 |
| 8130 | 3RD FLOOR BATHROOM TILE FLOOR | 4 | 4 | 0 | 24JUL08 | 29JUL08 | 0 |
| 8140 | 3RD FLOOR BATHROOM TILE WALLS | 5 | 5 | 0 | 30JUL08 | 05AUG08 | 0 |
| 8150 | 3RD FLOOR PRIME PAINT | 3 | 3 | 0 | 06AUG08 | 08AUG08 | 0 |
| 8160 | 3RD FLOOR PULL AND TERMINATE ELECTRICAL WIRE | 5 | 5 | 0 | 11AUG08 | 15AUG08 | 0 |
| 8170 | 3RD FLOOR CEILING GRID | 5 | 5 | 0 | 18AUG08 | 22AUG08 | 0 |
| 8180 | 3RD FLOOR OH LIGHT FIXTURES | 5 | 5 | 0 | 25AUG08 | 29AUG08 | 0 |
| 8190 | 3RD FLOOR SPRINKLER HEADS | 5 | 5 | 0 | 02SEP08 | 08SEP08 | 0 |
| 8210 | 3RD FLOOR ACOUSTICAL CEILING TILE | 2 | 2 | 0 | 09SEP08 | 10SEP08 | 0 |
| 8220 | 3RD FLOOR FINAL PAINT | 5 | 5 | 0 | 11SEP08 | 17SEP08 | 0 |
| 8230 | 3RD FLOOR CASEWORK | 5 | 5 | 0 | 18SEP08 | 24SEP08 | 0 |
| 8240 | 3RD FLOOR CHAIR RAILS AND MILLWORK ITEMS | 5 | 5 | 0 | 25SEP08 | 01OCT08 | 0 |
| 8260 | 3RD FLOOR CARPET | 5 | 5 | 0 | 02OCT08 | 08OCT08 | 0 |
| 8270 | 3RD FLOOR VCT AND SHEET VINYL | 5 | 5 | 0 | 02OCT08 | 08OCT08 | 0 |
| 8310 | 3RD FLOOR SPECIALTY ITEMS | 5 | 5 | 0 | 02OCT08 | 08OCT08 | 0 |
| 8440 | 3RD OPM PREPARE PUNCHLIST | 7 | 7 | 0 | 09OCT08 | 15OCT08 | 0 |
| 8690 | 3RD GARCETE PERFORM PUNCHLIST | 5 | 5 | 0 | 16OCT08 | 22OCT08 | 0 |
| 8700 | 3RD OPM RE-INSPECT PUNCHLIST | 3 | 3 | 0 | 23OCT08 | 27OCT08 | 0 |
| 790 | DEMOBILIZATION-BUILDING CONSTRUCTION CLEANUP | 2 | 2 | 0 | 24OCT08 | 27OCT08 | 0 |
| 70 | SUBSTANTIAL COMPLETION | 0 | 0 | 0 | | 27OCT08 | 0 |
| 740 | FINISH PROJECT PHOTOGRAPH | 1 | 1 | 0 | 27OCT08 | 27OCT08 | 0 |
| 8450 | 3RD FLOOR SUBSTANTIALLY COMPLETE | 0 | 0 | 0 | | 27OCT08 | 0 |
| 800 | DEMOBILIZATION-TRAILER REMOVAL | 2 | 2 | 0 | 28OCT08 | 29OCT08 | 0 |
| 810 | DEMOBILIZATION-DISCONNECT TEMP. UTILITIES | 2 | 2 | 0 | 30OCT08 | 31OCT08 | 0 |
| 820 | DEMOBILIZATION-SITE CLEANUP | 5 | 5 | 0 | 03NOV08 | 07NOV08 | 0 |

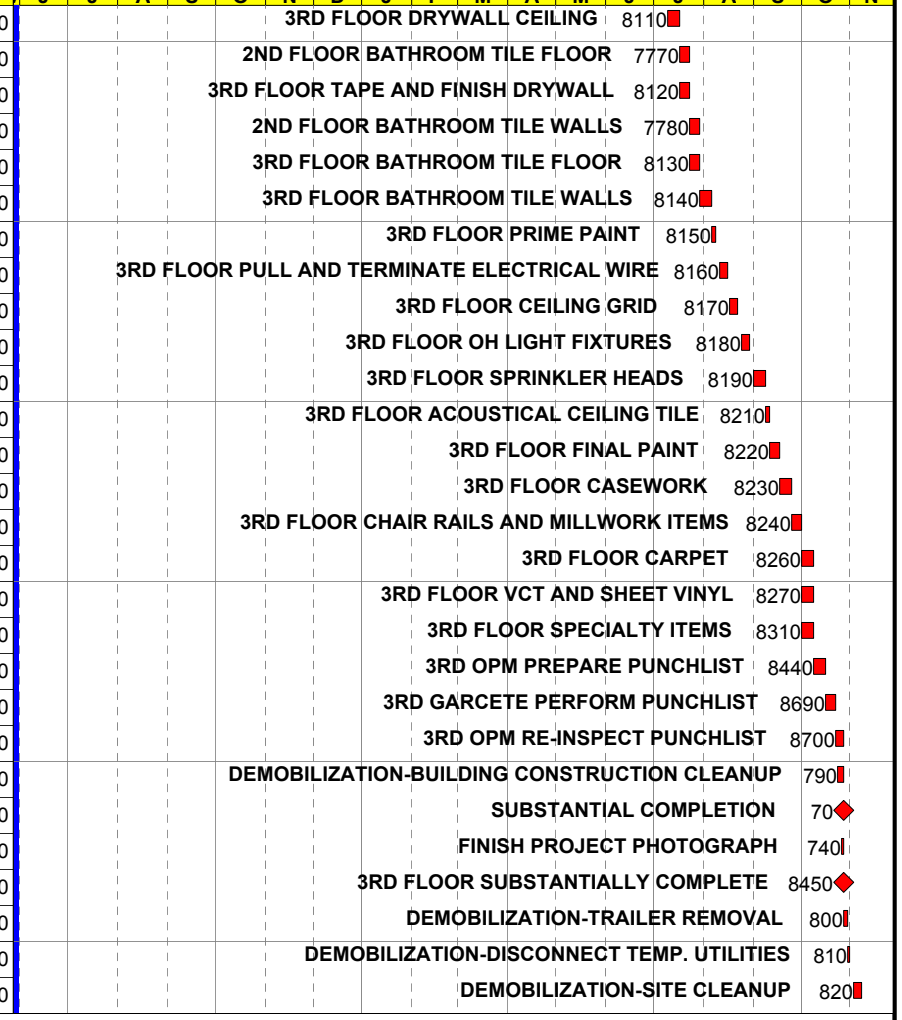


| | |
|---|---|
| Start Date | 01MAY07 |
| Finish Date | 07NOV08 |
| Data Date | 29MAY07 |
| Run Date | 21MAR08 13:19 |

Early Bar
Progress Bar
Critical Activity

WC00

Sheet 3 of 3

**SIMSONA CORP.**

**SENIOR WELLNESS CENTER - WARD 1**
**BASELINE**
**LONGEST PATH**

| Date | Revision | Checked | Approved |
|---|---|---|---|
| | | | |

© Primavera Systems, Inc.
